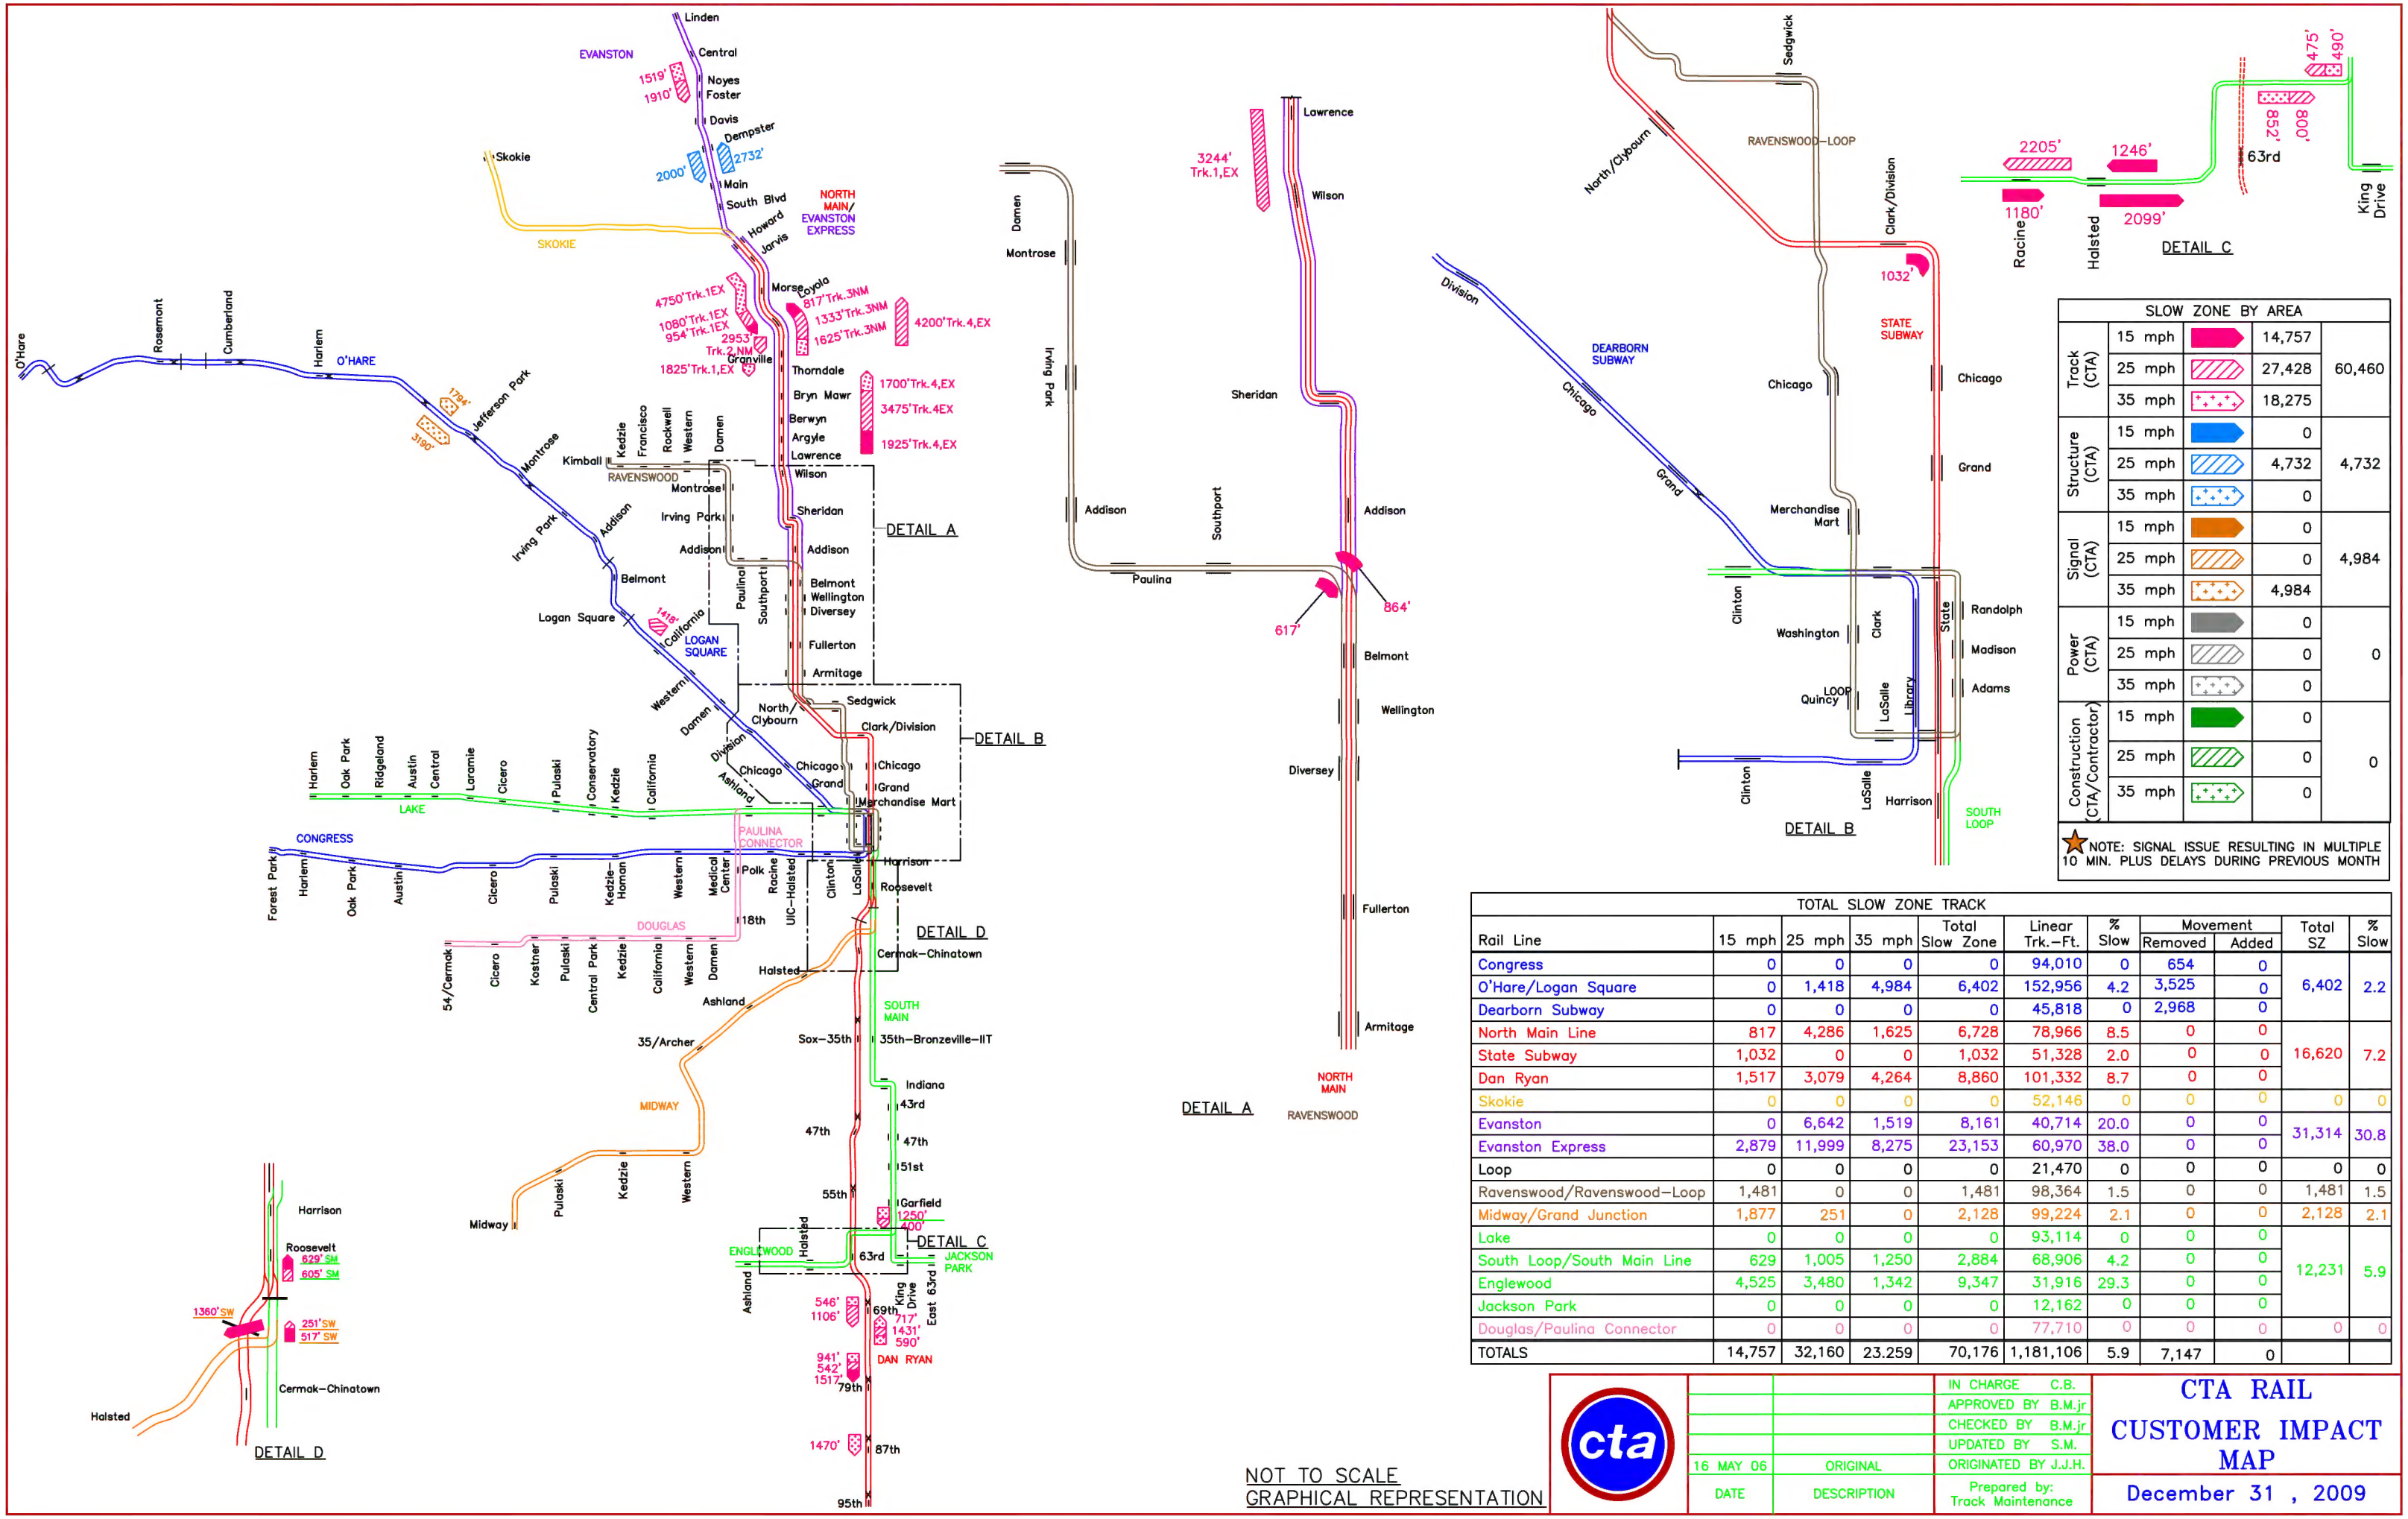


| SLOW ZONE BY AREA | | | | |
|---|---|---|---|---|
| Track (CTA) | 15 mph | | 14,757 | 60,460 |
| | 25 mph | | 27,428 | |
| | 35 mph | | 18,275 | |
| Structure (CTA) | 15 mph | | 0 | 4,732 |
| | 25 mph | | 4,732 | |
| | 35 mph | | 0 | |
| Signal (CTA) | 15 mph | | 0 | 4,984 |
| | 25 mph | | 0 | |
| | 35 mph | | 4,984 | |
| Power (CTA) | 15 mph | | 0 | 0 |
| | 25 mph | | 0 | |
| | 35 mph | | 0 | |
| Construction (CTA/Contractor) | 15 mph | | 0 | 0 |
| | 25 mph | | 0 | |
| | 35 mph | | 0 | |

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

| TOTAL SLOW ZONE TRACK | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|
| Rail Line | 15 mph | 25 mph | 35 mph | Total Slow Zone | Linear Trk.–Ft. | % Slow | Movement Removed | Movement Added | Total SZ | % Slow |
| Congress | 0 | 0 | 0 | 0 | 94,010 | 0 | 654 | 0 | 6,402 | 2.2 |
| O'Hare/Logan Square | 0 | 1,418 | 4,984 | 6,402 | 152,956 | 4.2 | 3,525 | 0 | | |
| Dearborn Subway | 0 | 0 | 0 | 0 | 45,818 | 0 | 2,968 | 0 | | |
| North Main Line | 817 | 4,286 | 1,625 | 6,728 | 78,966 | 8.5 | 0 | 0 | 16,620 | 7.2 |
| State Subway | 1,032 | 0 | 0 | 1,032 | 51,328 | 2.0 | 0 | 0 | | |
| Dan Ryan | 1,517 | 3,079 | 4,264 | 8,860 | 101,332 | 8.7 | 0 | 0 | | |
| Skokie | 0 | 0 | 0 | 0 | 52,146 | 0 | 0 | 0 | 0 | 0 |
| Evanston | 0 | 6,642 | 1,519 | 8,161 | 40,714 | 20.0 | 0 | 0 | 31,314 | 30.8 |
| Evanston Express | 2,879 | 11,999 | 8,275 | 23,153 | 60,970 | 38.0 | 0 | 0 | | |
| Loop | 0 | 0 | 0 | 0 | 21,470 | 0 | 0 | 0 | 0 | 0 |
| Ravenswood/Ravenswood–Loop | 1,481 | 0 | 0 | 1,481 | 98,364 | 1.5 | 0 | 0 | 1,481 | 1.5 |
| Midway/Grand Junction | 1,877 | 251 | 0 | 2,128 | 99,224 | 2.1 | 0 | 0 | 2,128 | 2.1 |
| Lake | 0 | 0 | 0 | 0 | 93,114 | 0 | 0 | 0 | 12,231 | 5.9 |
| South Loop/South Main Line | 629 | 1,005 | 1,250 | 2,884 | 68,906 | 4.2 | 0 | 0 | | |
| Englewood | 4,525 | 3,480 | 1,342 | 9,347 | 31,916 | 29.3 | 0 | 0 | | |
| Jackson Park | 0 | 0 | 0 | 0 | 12,162 | 0 | 0 | 0 | | |
| Douglas/Paulina Connector | 0 | 0 | 0 | 0 | 77,710 | 0 | 0 | 0 | 0 | 0 |
| TOTALS | 14,757 | 32,160 | 23.259 | 70,176 | 1,181,106 | 5.9 | 7,147 | 0 | | |

NOT TO SCALE
GRAPHICAL REPRESENTATION

| | | | |
|---|---|---|---|
| | | IN CHARGE C.B. | CTA RAIL CUSTOMER IMPACT MAP |
| | | APPROVED BY B.M.jr | |
| | | CHECKED BY B.M.jr | |
| | | UPDATED BY S.M. | |
| 16 MAY 06 | ORIGINAL | ORIGINATED BY J.J.H. | |
| DATE | DESCRIPTION | Prepared by: Track Maintenance | December 31 , 2009 |
